



Great Neck Library
Schedule



Task	Summary	External Milestone	Inactive Milestone	Duration-only	Start-only	External Milestone
Split	Project Summary	Inactive Task	Inactive Summary	Manual Summary Rollup	Finish-only	Progress
Milestone	External Tasks	Inactive Milestone	Manual Task	Manual Summary	External Tasks	Deadline


Great Neck Library
Schedule



Project: GNL Schedule 7.14.15====+8 Date: Thu 8/6/15	Task	Summary	External Milestone	Inactive Milestone	Duration-only	Start-only	External Milestone
	Split	Project Summary	Inactive Task	Inactive Summary	Manual Summary Rollup	Finish-only	Progress
	Milestone	External Tasks	Inactive Milestone	Manual Task	Manual Summary	External Tasks	Deadline

Great Neck Library
Schedule

ID	Task Name	Duration	Start	Finish	Predecessors	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March	April	May	June	July	August	September	October	November
104	Lighting Control Panel Installation	5 days	Mon 12/14/15	Fri 12/18/15																								
112	Basement Painting	10 days	Mon 12/14/15	Fri 12/25/15	109,111																							
113	Basement HVAC Drops	15 days	Mon 12/14/15	Fri 1/1/16	111																							
117	Basement Bathrooms Ceramic Tile	10 days	Mon 12/14/15	Fri 12/25/15	111																							
68	Exterior Window Removals	20 days	Mon 12/21/15	Fri 1/15/16	67																							
105	Lighting Control Panel Wiring Lower Level	10 days	Mon 12/21/15	Fri 1/1/16	104																							
118	Basement Bathroom Toilets/Sinks	5 days	Mon 12/28/15	Fri 1/1/16	117																							
128	Main Level Painting	15 days	Thu 12/31/15	Wed 1/20/16	127																							
129	Main Level HVAC Drops	15 days	Thu 12/31/15	Wed 1/20/16	127																							
131	Main Level Fire Sprinkler Drops	10 days	Thu 12/31/15	Wed 1/13/16	127																							
133	Main Level Bathroom Ceramic Tile	10 days	Thu 12/31/15	Wed 1/13/16	127																							
173	Asphalt Repair	3 days	Fri 1/1/16	Tue 1/5/16	172																							
106	Lighting Control Panel Wiring Main Level	10 days	Mon 1/4/16	Fri 1/15/16	105																							
116	Basement Ceiling Tiles	20 days	Mon 1/4/16	Fri 1/29/16	111,113,115																							
119	Basement Bathroom Partitions	4 days	Mon 1/4/16	Thu 1/7/16	118																							
174	Light Pole Installation	5 days	Wed 1/6/16	Tue 1/12/16	170FS+20 days																							
120	Basement Bathroom Toilet Accessories	2 days	Fri 1/8/16	Mon 1/11/16	119																							
134	Main Level Bathroom Toilets/Sinks	5 days	Thu 1/14/16	Wed 1/20/16	133																							
107	Lighting Control Panel Wiring Mezzanine	1 day	Mon 1/18/16	Mon 1/18/16	106																							
132	Main Level Ceiling Tiles	20 days	Thu 1/21/16	Wed 2/17/16	127,129,131																							
135	Main Level Bathroom Partitions	5 days	Thu 1/21/16	Wed 1/27/16	134																							
136	Main Level Bathroom Toilet Accessories	2 days	Thu 1/28/16	Fri 1/29/16	135																							
121	Basement Level Carpet and VCT	15 days	Mon 2/1/16	Fri 2/19/16	116																							
176	Asphalt Lot Overlay	4 days	Fri 2/12/16	Wed 2/17/16	175FS+40 days																							
137	Main Level Carpet	20 days	Thu 2/18/16	Wed 3/16/16	132																							
122	Basement Level Millwork	15 days	Mon 2/22/16	Fri 3/11/16	121																							
123	Basement Level Doors and Hardware	10 days	Mon 2/22/16	Fri 3/4/16	121																							
177	Asphalt Striping	2 days	Thu 2/25/16	Fri 2/26/16	176FS+5 days																							
178	Site Signage	3 days	Mon 2/29/16	Wed 3/2/16	177																							
138	Main Level Millwork	20 days	Thu 3/17/16	Wed 4/13/16	137																							
139	Main Level Doors and Hardware	20 days	Thu 3/17/16	Wed 4/13/16	137																							
140	Misc. Furnishings	20 days	Thu 4/14/16	Wed 5/11/16	139																							
141	Substantial Completion	23 days	Fri 4/22/16	Tue 5/24/16	18FS+240 days																							
142	Punchlist	23 days	Fri 4/22/16	Tue 5/24/16																								

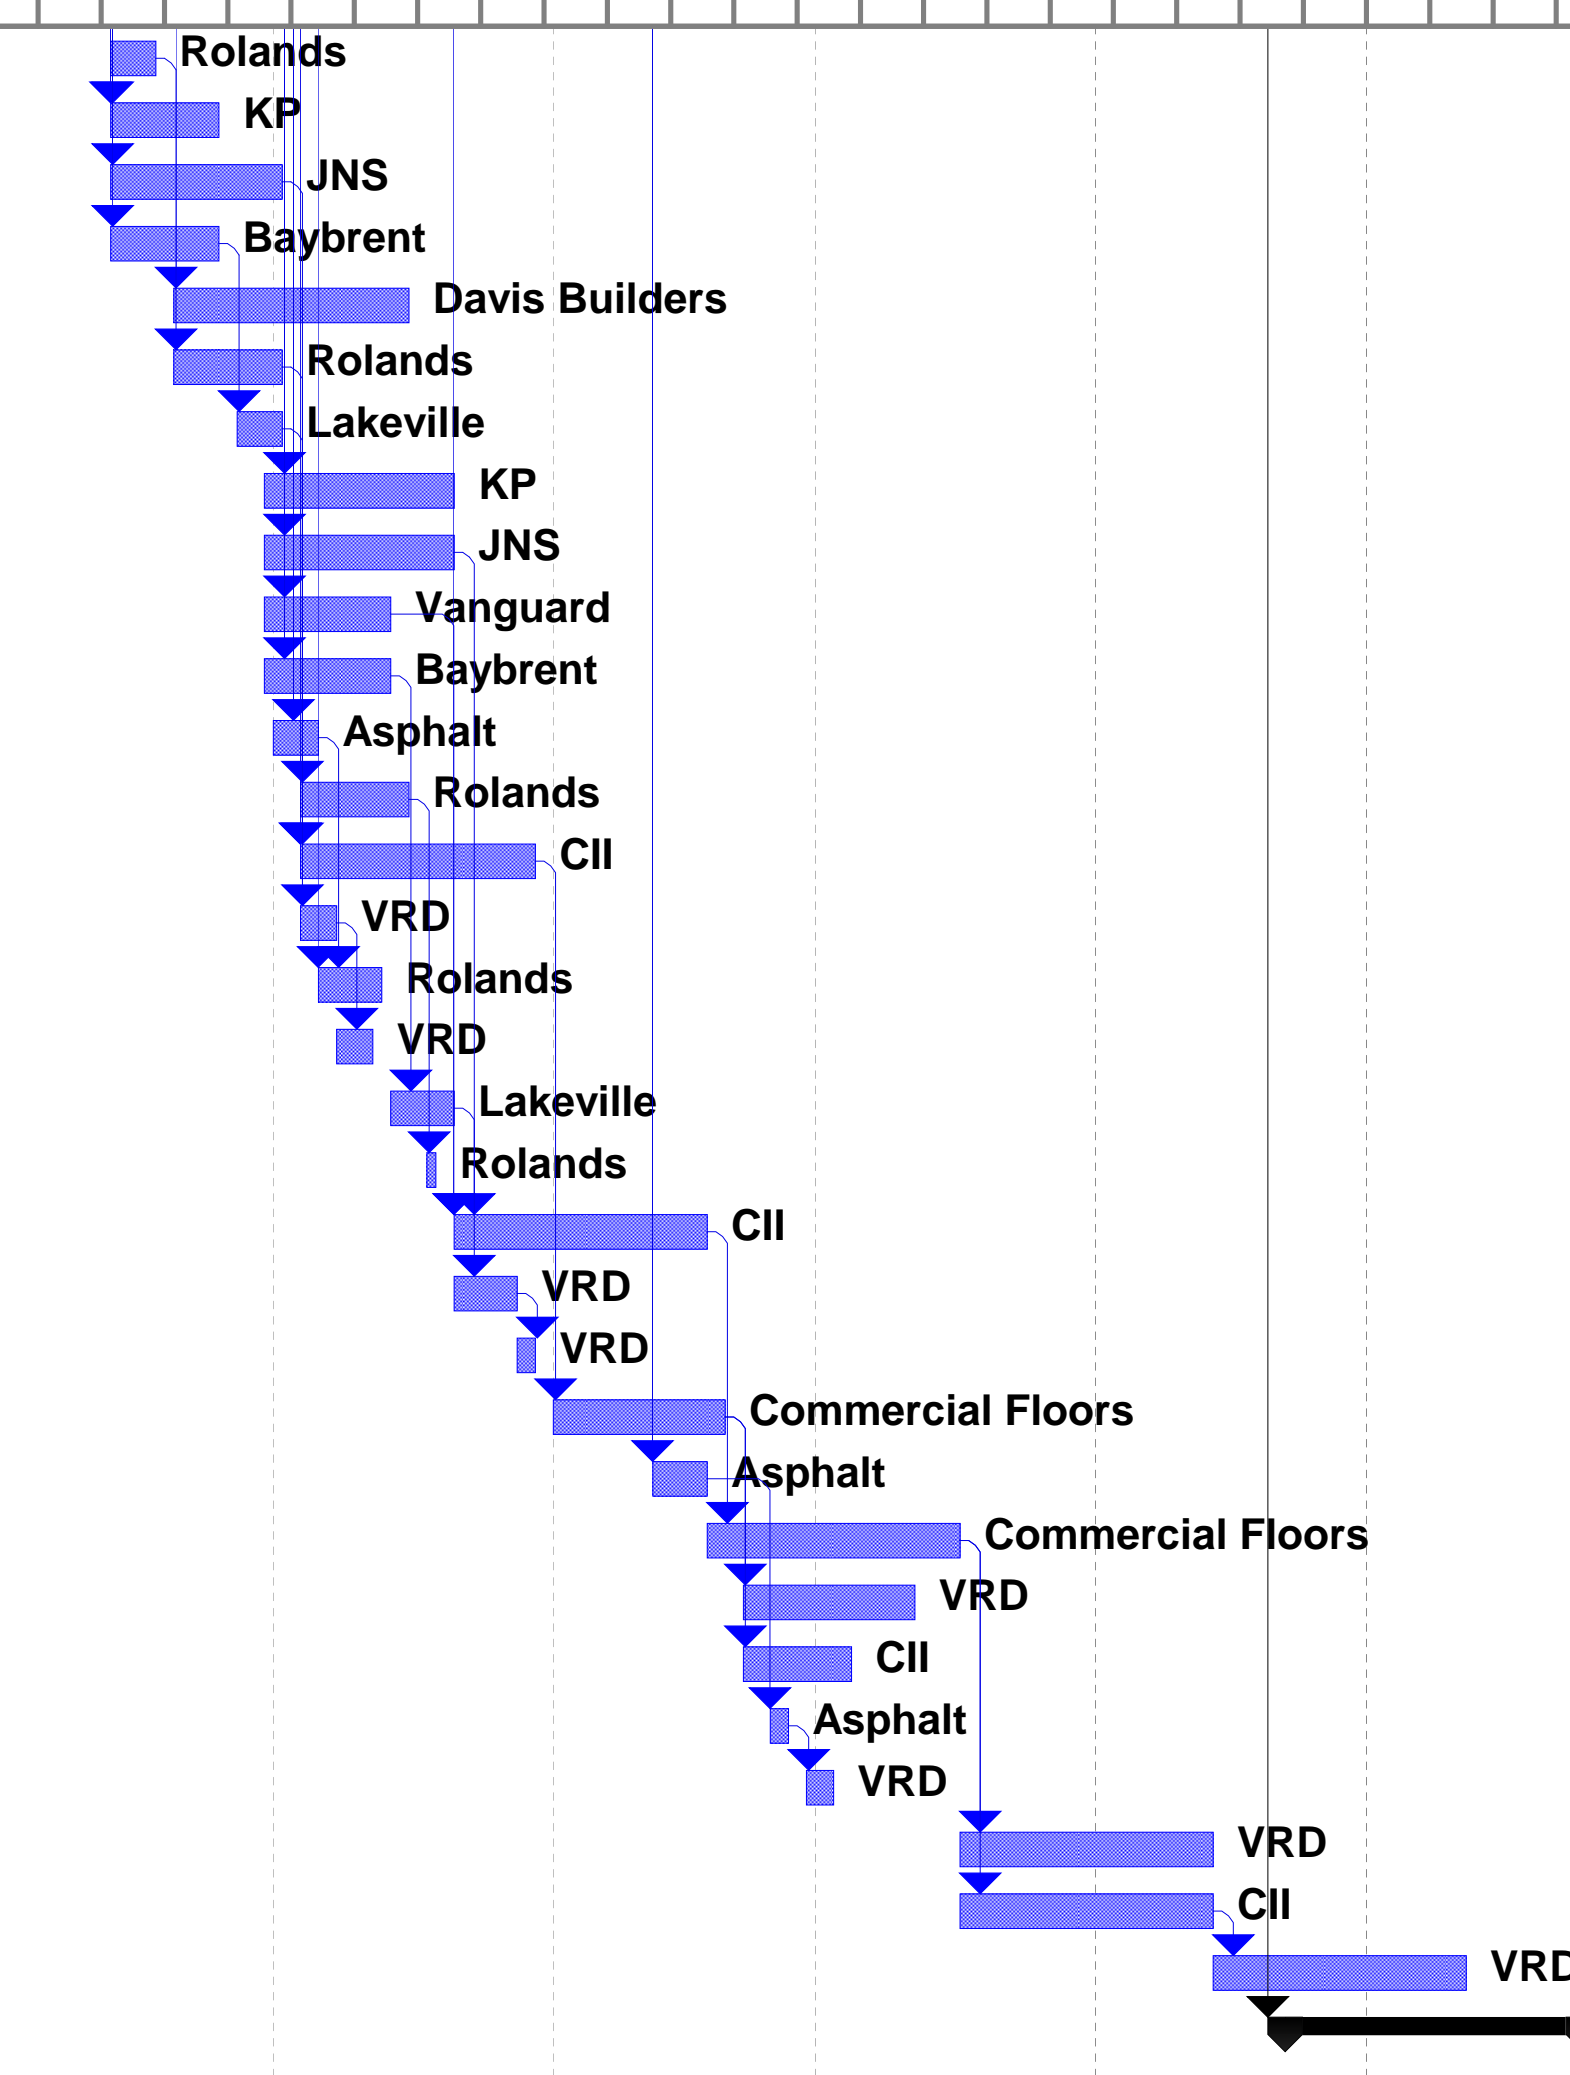

Project: GNL Schedule 7.14.15====+8 Date: Thu 8/6/15	Task	Summary	External Milestone	Inactive Milestone	Duration-only	Start-only	External Milestone
	Split	Project Summary	Inactive Task	Inactive Summary	Manual Summary Rollup	Finish-only	Progress
	Milestone	External Tasks	Inactive Milestone	Manual Task	Manual Summary	External Tasks	Deadline
